


Project ID:	P039718	County:	Richland	Boring No.:	36-End Bent 1 LT
Site Description:	Carolina Crossroads Phase 1 - Bridge 36			Route:	Bridge 36
Eng./Geo.:	CM & NM	Boring Location:	30+01	Offset:	26 LT
Elev.:	183.0 ft	Latitude:	34.02168598	Longitude:	-81.09596711
Date Started:	11/16/2021				
Total Depth:	40.2 ft	Soil Depth:	20.2 ft	Core Depth:	20 ft
Date Completed:	11/16/2021				
Bore Hole Diameter (in):	2.25	Sampler Configuration		Liner Required:	Y (N)
Liner Used:	Y (N)				
Drill Machine:	D-50 #0435	Drill Method:	Casing w/ Adv	Hammer Type:	Automatic
Energy Ratio:	84%				
Core Size:	NQ2	Driller:	M. Morgan	Groundwater:	TOB NM
24HR:	6.8 ft				

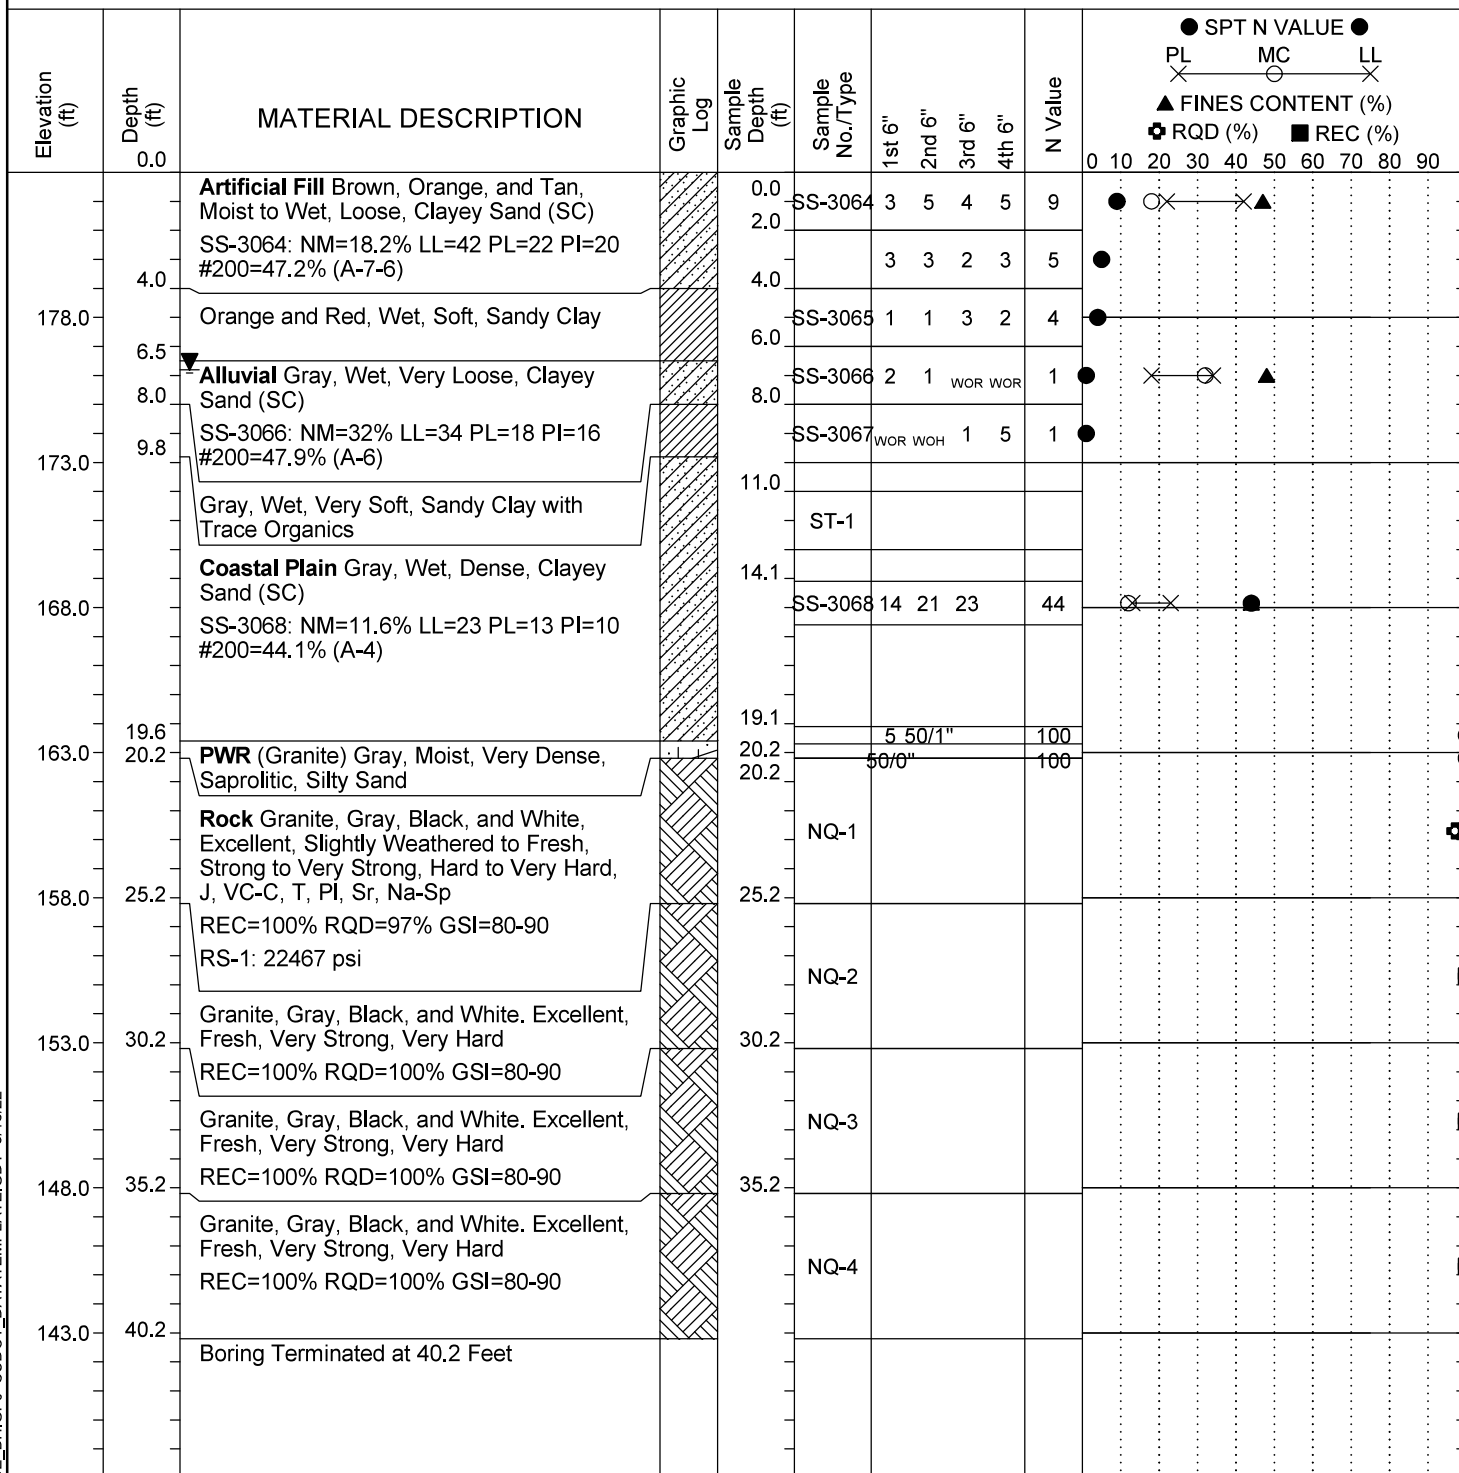

LEGEND

SAMPLER TYPE		DRILLING METHOD	
SS - Split Spoon	NQ - Rock Core, 1-7/8"	HSA - Hollow Stem Auger	RW - Rotary Wash
UD - Undisturbed Sample	CU - Cuttings	CFA - Continuous Flight Augers	RC - Rock Core
AWG - Rock Core, 1-1/8"	CT - Continuous Tube	DC - Driving Casing	
